

# McCownGordon Construction

## PROJECT MONTHLY UPDATE

---

### Sunflower Fire Station

10/31/24

### SUMMARY

This is a monthly construction update that is designed to keep everyone informed of the current Project status. Please feel free to reach out with any questions.


*Capping the rock excavation with clay and profiling the banks at 102<sup>nd</sup> Street*



CONFIDENTIAL WORK PRODUCT – COPYRIGHT 2024 | McCownGordon Construction, LLC, All Rights Reserved

**McCownGordon**  
CONSTRUCTION



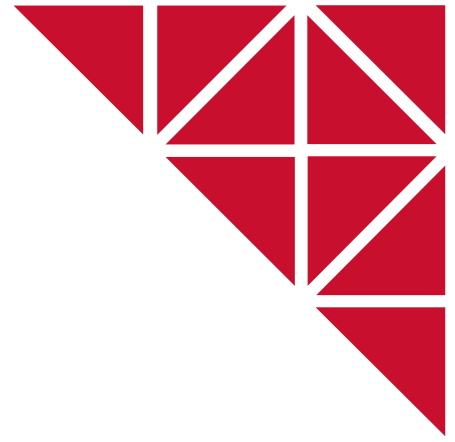

*Final rock excavation at road elevation completed and fenced on 10/10/24*



*Vapor barrier and mud sill install beneath the trench drains at the App Bay*



*Under slab electric complete, foam installed, 4" granular course installed, first course CMU installed*



*Finalizing rebar and vapor barrier before the pour*



CONFIDENTIAL WORK PRODUCT – COPYRIGHT 2024 | McCownGordon Construction, LLC, All Rights Reserved

**McCOWNGORDON**  
CONSTRUCTION





*App Bay slab poured, finished and sawcut*



*Drone Photo Overall Site Progress*



Weather Days this month:

- 1 weather days for the month of October.

Activities planned for the next month:

- Start and complete storm water utilities along Lexington
- Start storm water utilities on 102<sup>nd</sup> Street
- Erect West CMU wall at App Bay
- Start erecting walls at SCBA and Decon rooms
- Complete under slab utilities at Living Quarters
- Pour slab at Living Quarters

-The McCownGordon Team
